





2024 Joint Agency Slurry Seal Project Map 24-A

- DAY 1 - MONDAY, JULY 8TH**
- DAY 2 - TUESDAY, JULY 9TH**
- DAY 3 - WEDNESDAY, JULY 10TH**
- DAY 4 - THURSDAY, JULY 11TH**
- DAY 5 - FRIDAY, JULY 12TH**

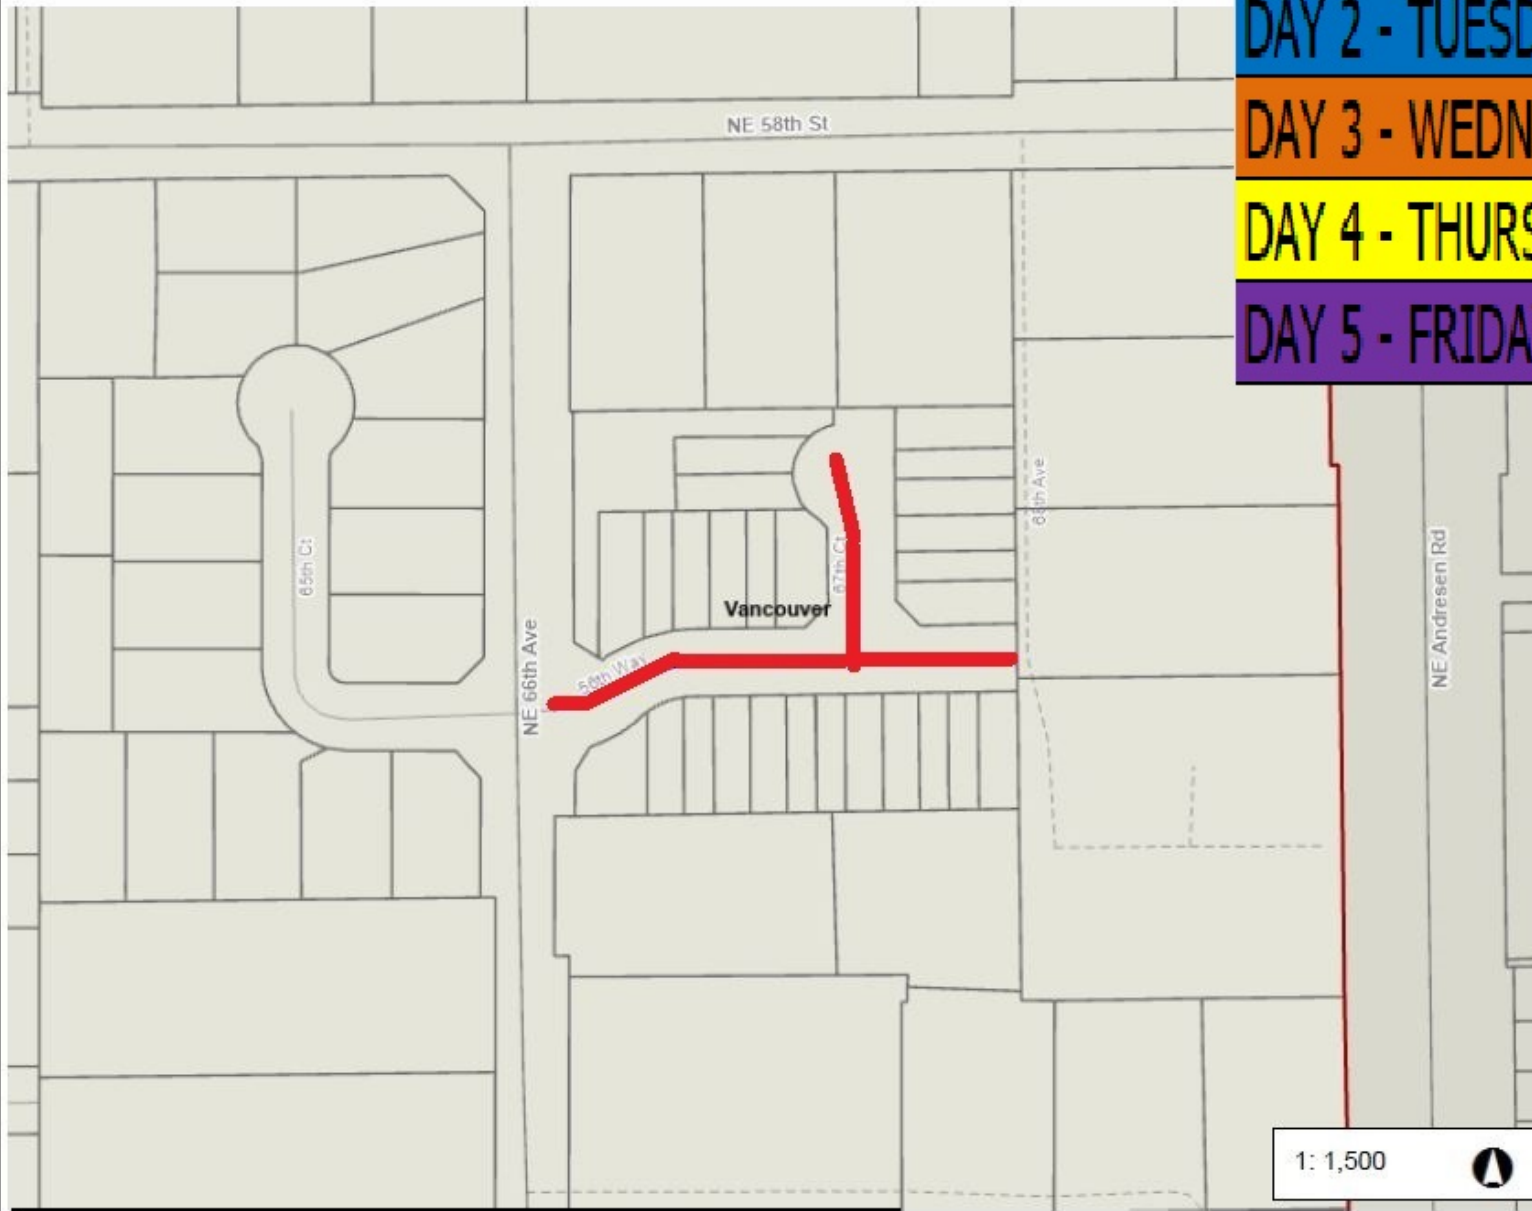

SUBDIVISIONS: 311578 - STONESTHROW AT WESTFIELD

1: 1,500

FRIDAY GARBAGE

This map was generated by Clark County's "MapsOnline" website. Clark County does not warrant the accuracy, reliability or timeliness of any information on this map, and shall not be held liable for losses caused by using this information.



2024 Joint Agency Slurry Seal Project Map 24-B


DAY 1 - MONDAY, JULY 8TH

DAY 2 - TUESDAY, JULY 9TH

DAY 3 - WEDNESDAY, JULY 10TH

DAY 4 - THURSDAY, JULY 11TH

DAY 5 - FRIDAY, JULY 12TH

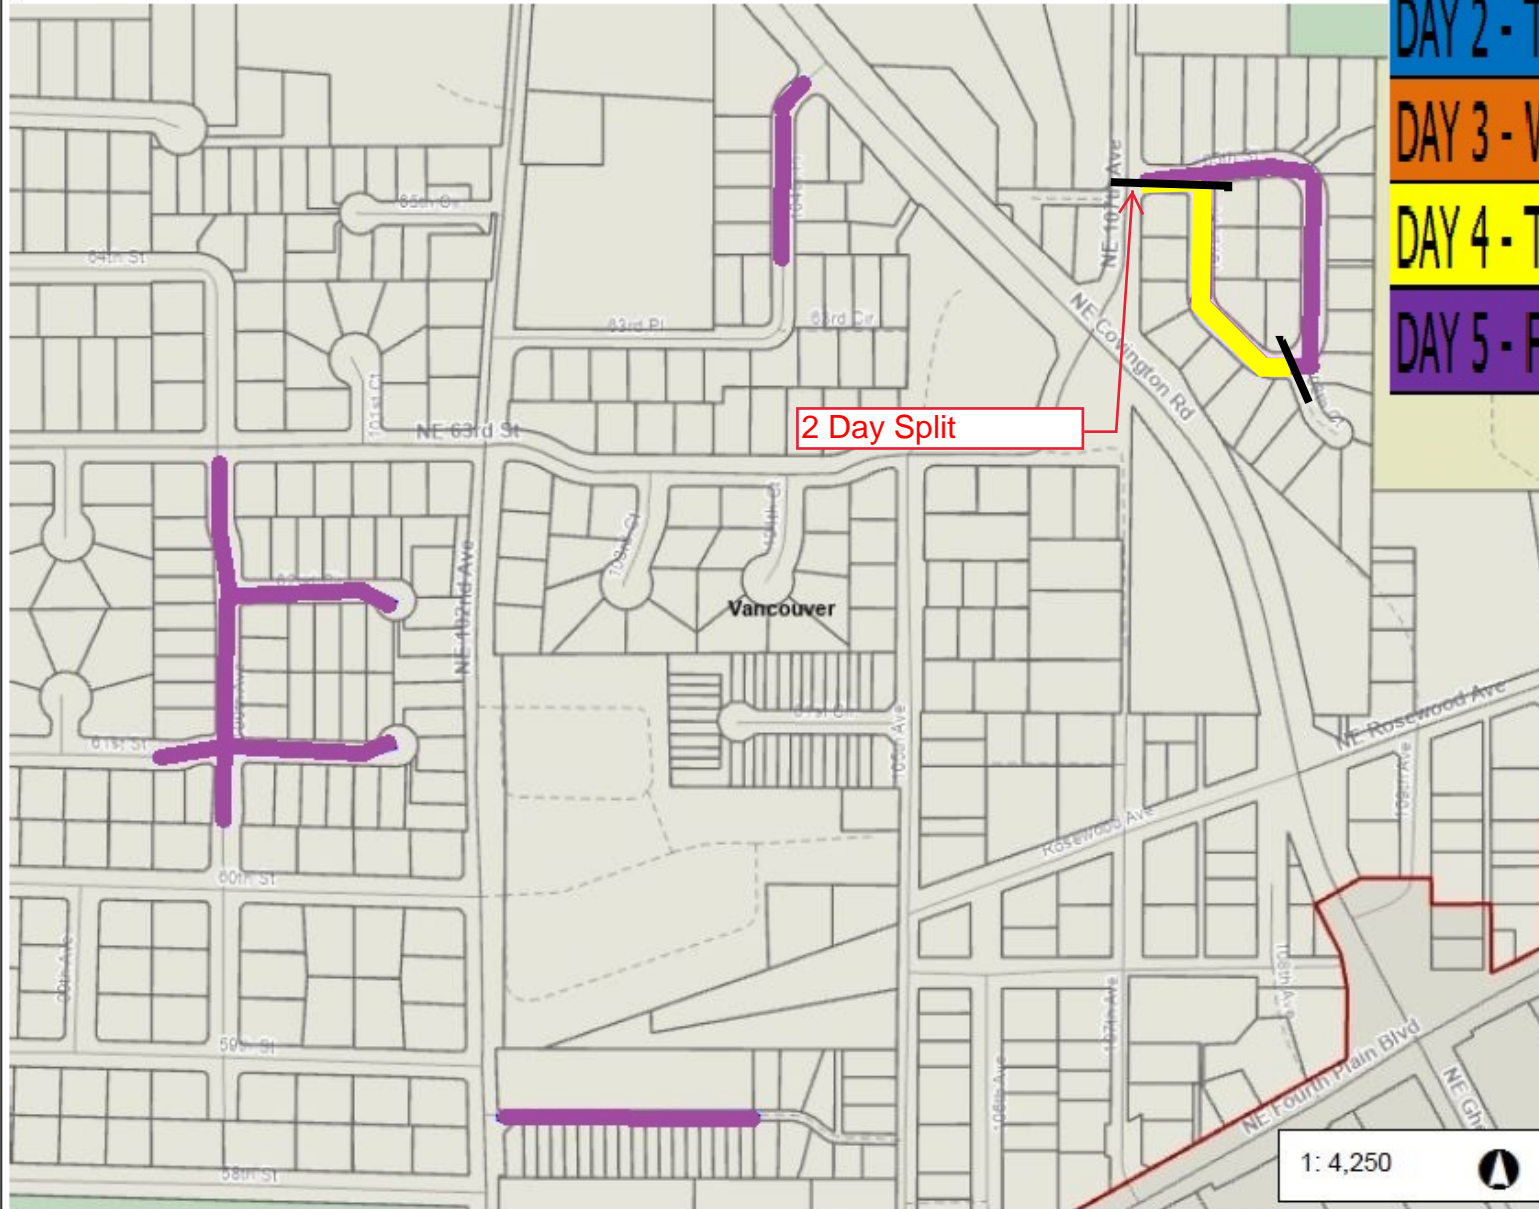

2 Day Split

Vancouver

1: 4,250



SUBDIVISIONS:
 J50 - ORCHARDS MEADOW
 ESTATES PHASE II
 310595 - FRONTIS 2
 H130 - FRONTIS
 311327 - ORCHARDS PARK 2
 311019 - CONVINGTON MANOR

WEDNESDAY GARBAGE



2024 Joint Agency Slurry Seal Project Map 24-C


DAY 1 - MONDAY, JULY 8TH

DAY 2 - TUESDAY, JULY 9TH

DAY 3 - WEDNESDAY, JULY 10TH

DAY 4 - THURSDAY, JULY 11TH

DAY 5 - FRIDAY, JULY 12TH

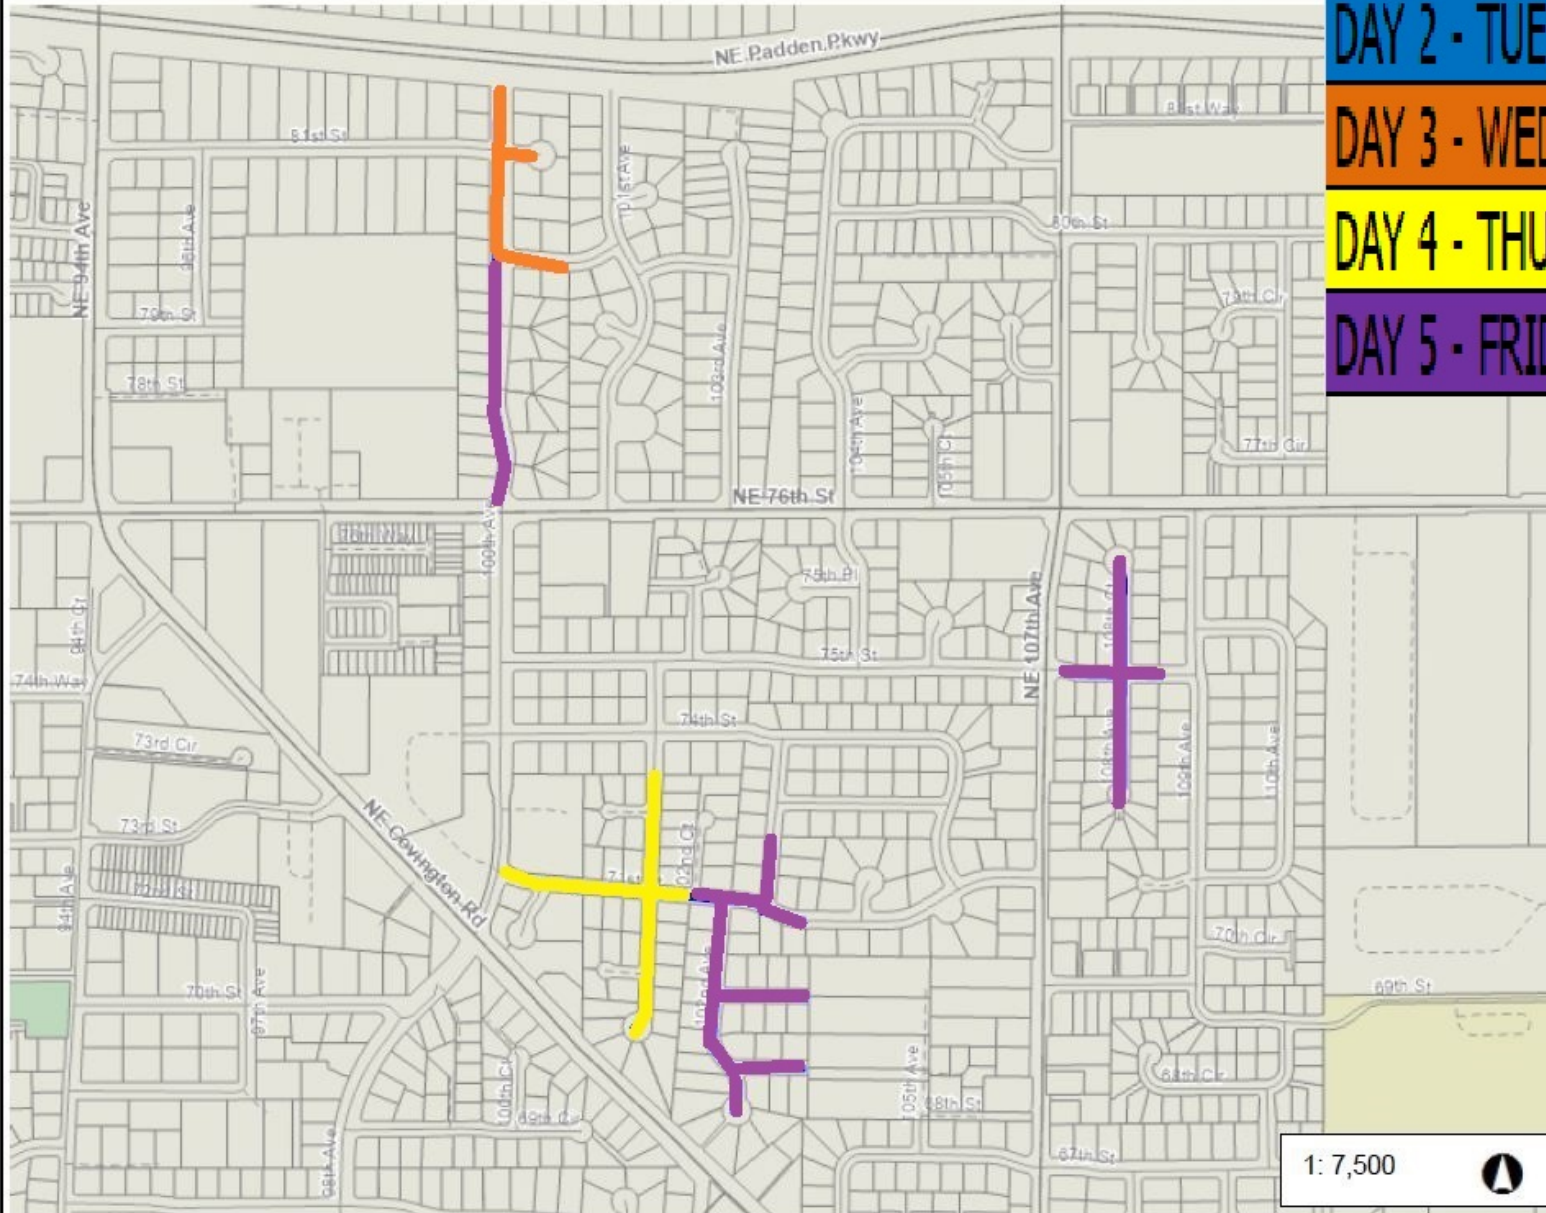

1: 7,500



WEDNESDAY GARBAGE

- SUBDIVISIONS:
- H615 - ORCHARDS MEADOWS ESTATES
 - 3-877 - MICHA'S PLACE SHORT PLAT
 - H746 - MESA VERDE 3
 - H544 - SUNNY MEADOWS
 - G553 - DIAMOND WILLOW
 - H543 - KINGS LAND




DAY 1 - MONDAY, JULY 8TH

DAY 2 - TUESDAY, JULY 9TH

DAY 3 - WEDNESDAY, JULY 10TH

DAY 4 - THURSDAY, JULY 11TH

DAY 5 - FRIDAY, JULY 12TH

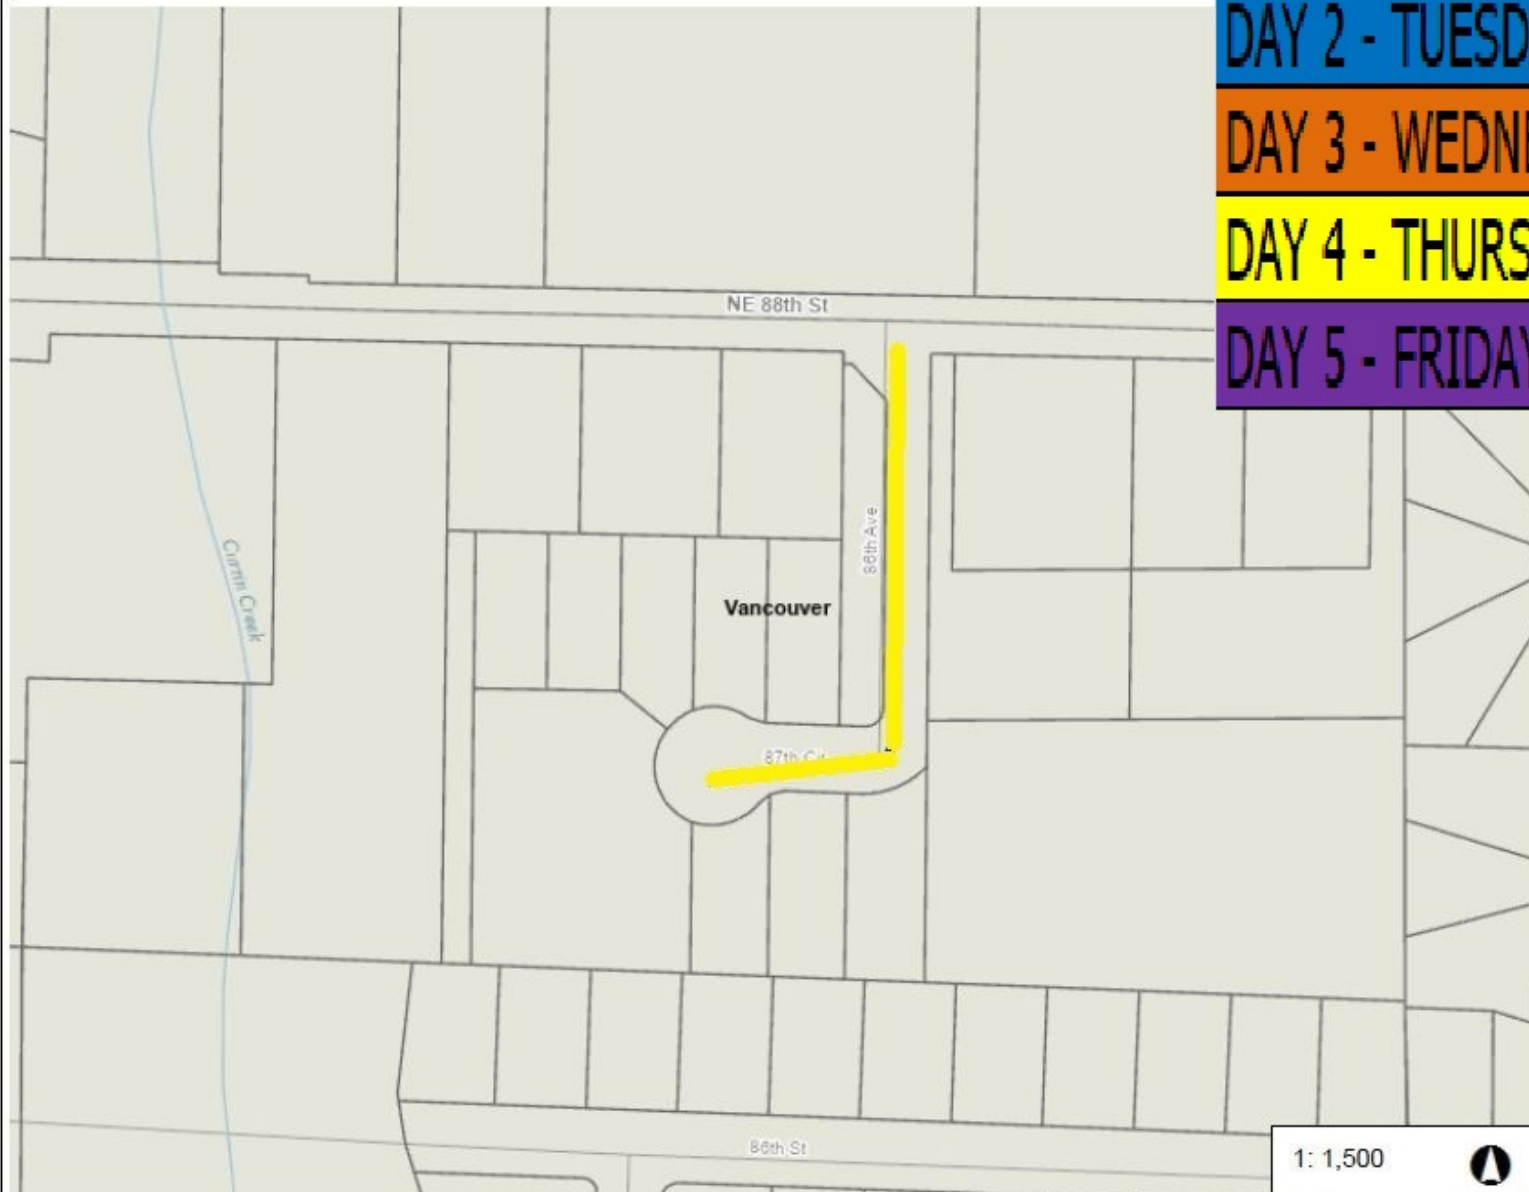

SUBDIVISIONS:
311694 - HESS SUBDIVISION PH 1

1: 1,500

WEDNESDAY GARBAGE



2024 Joint Agency Slurry Seal Project Map 24-E



DAY 1 - MONDAY, JULY 8TH

DAY 2 - TUESDAY, JULY 9TH

DAY 3 - WEDNESDAY, JULY 10TH

DAY 4 - THURSDAY, JULY 11TH

DAY 5 - FRIDAY, JULY 12TH

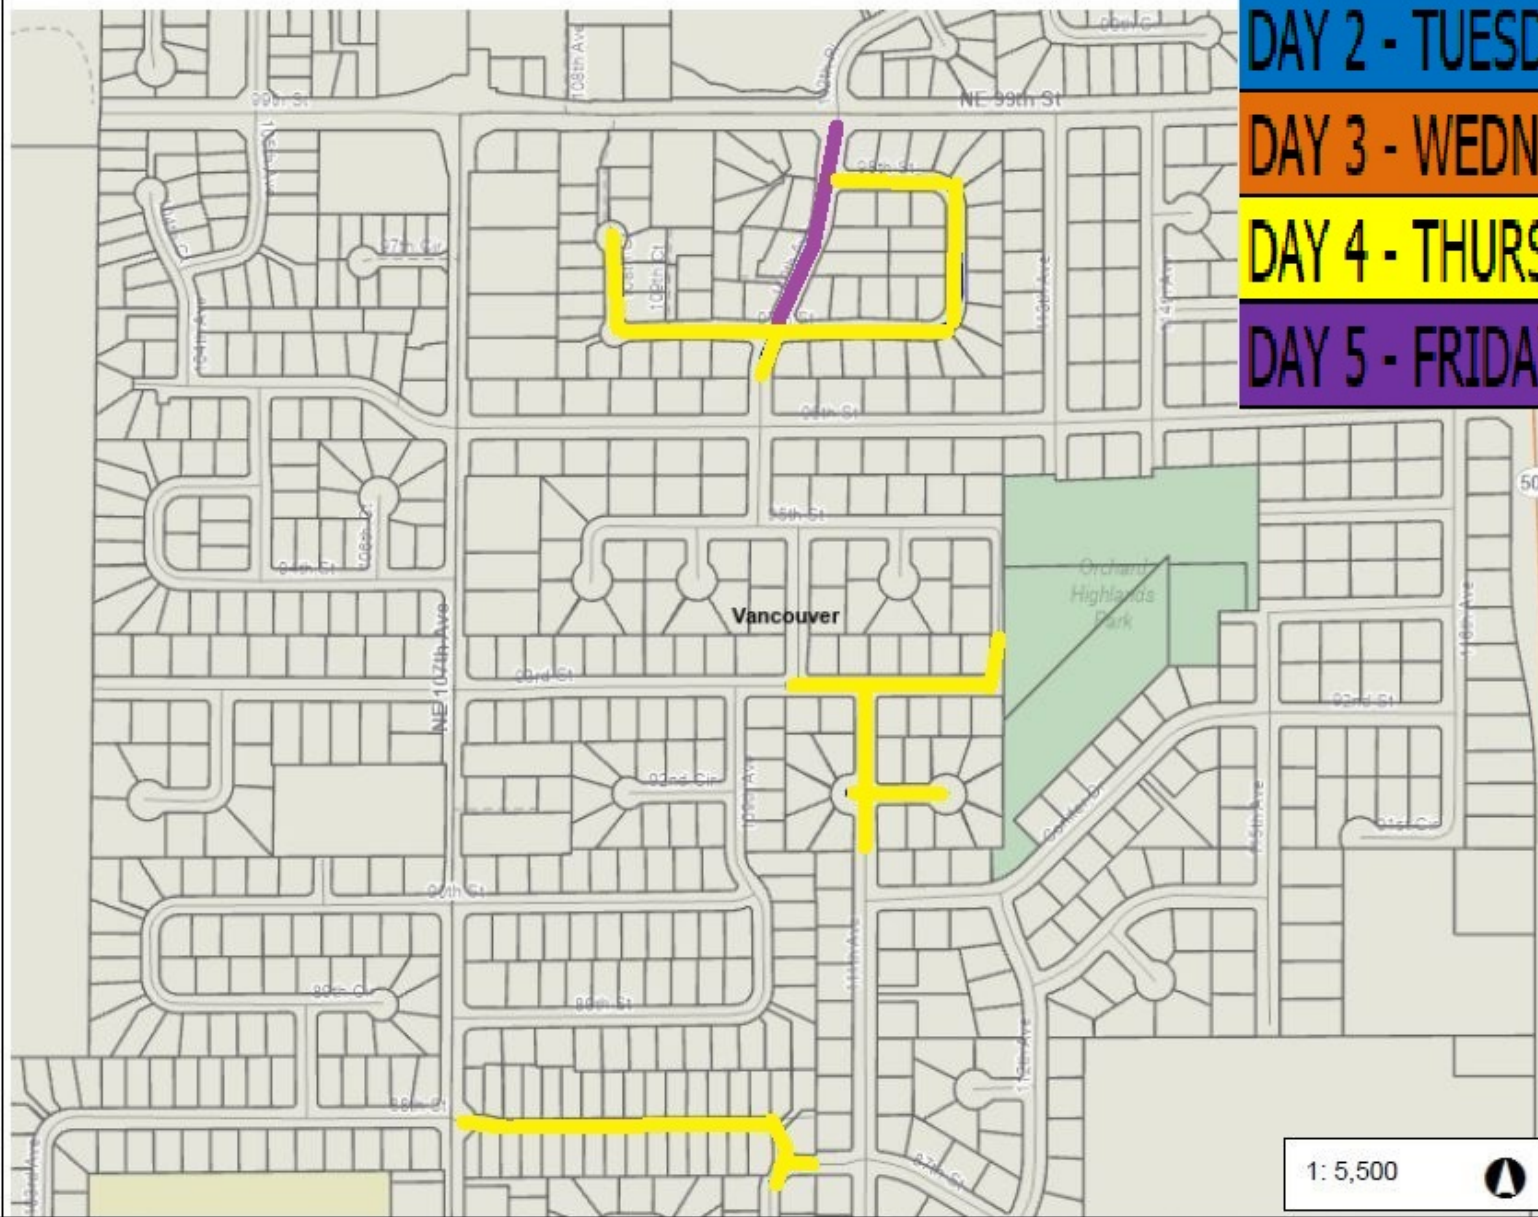

SUBDIVISIONS:
 H875 - FLAHERTY WOODS
 3-865 - SHYANNES CORRAL 1
 H703 - COUNTRY MEADOWS
 311391 - JULIAS GARDEN

1: 5,500

WEDNESDAY GARBAGE



2024 Joint Agency Slurry Seal Project Map 24-F


DAY 1 - MONDAY, JULY 8TH

DAY 2 - TUESDAY, JULY 9TH

DAY 3 - WEDNESDAY, JULY 10TH

DAY 4 - THURSDAY, JULY 11TH

DAY 5 - FRIDAY, JULY 12TH

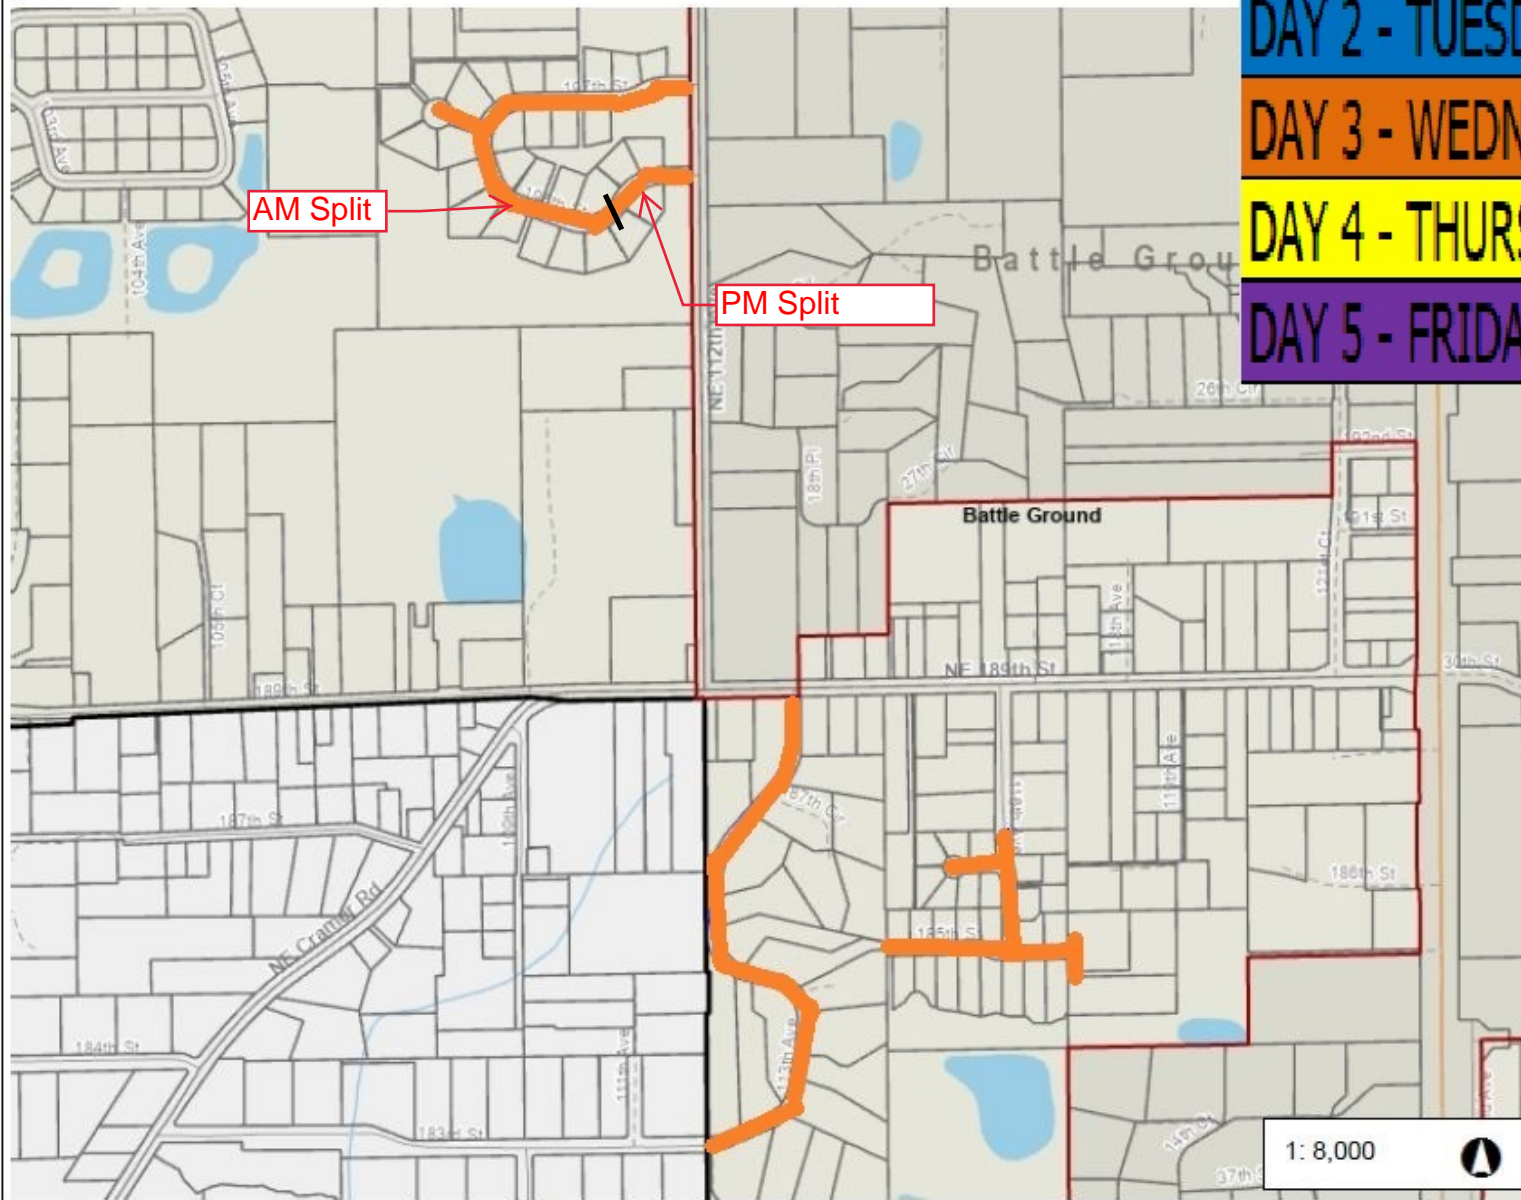

SUBDIVISIONS:
 311511 - WHISPERING MEADOWS PH 2
 J404 - LARSEN MEADOWS
 J402 - MEADOWLAND ESTATES

1: 8,000

FRIDAY GARBAGE



2024 Joint Agency Slurry Seal Project Map 24-G


DAY 1 - MONDAY, JULY 8TH

DAY 2 - TUESDAY, JULY 9TH

DAY 3 - WEDNESDAY, JULY 10TH

DAY 4 - THURSDAY, JULY 11TH

DAY 5 - FRIDAY, JULY 12TH

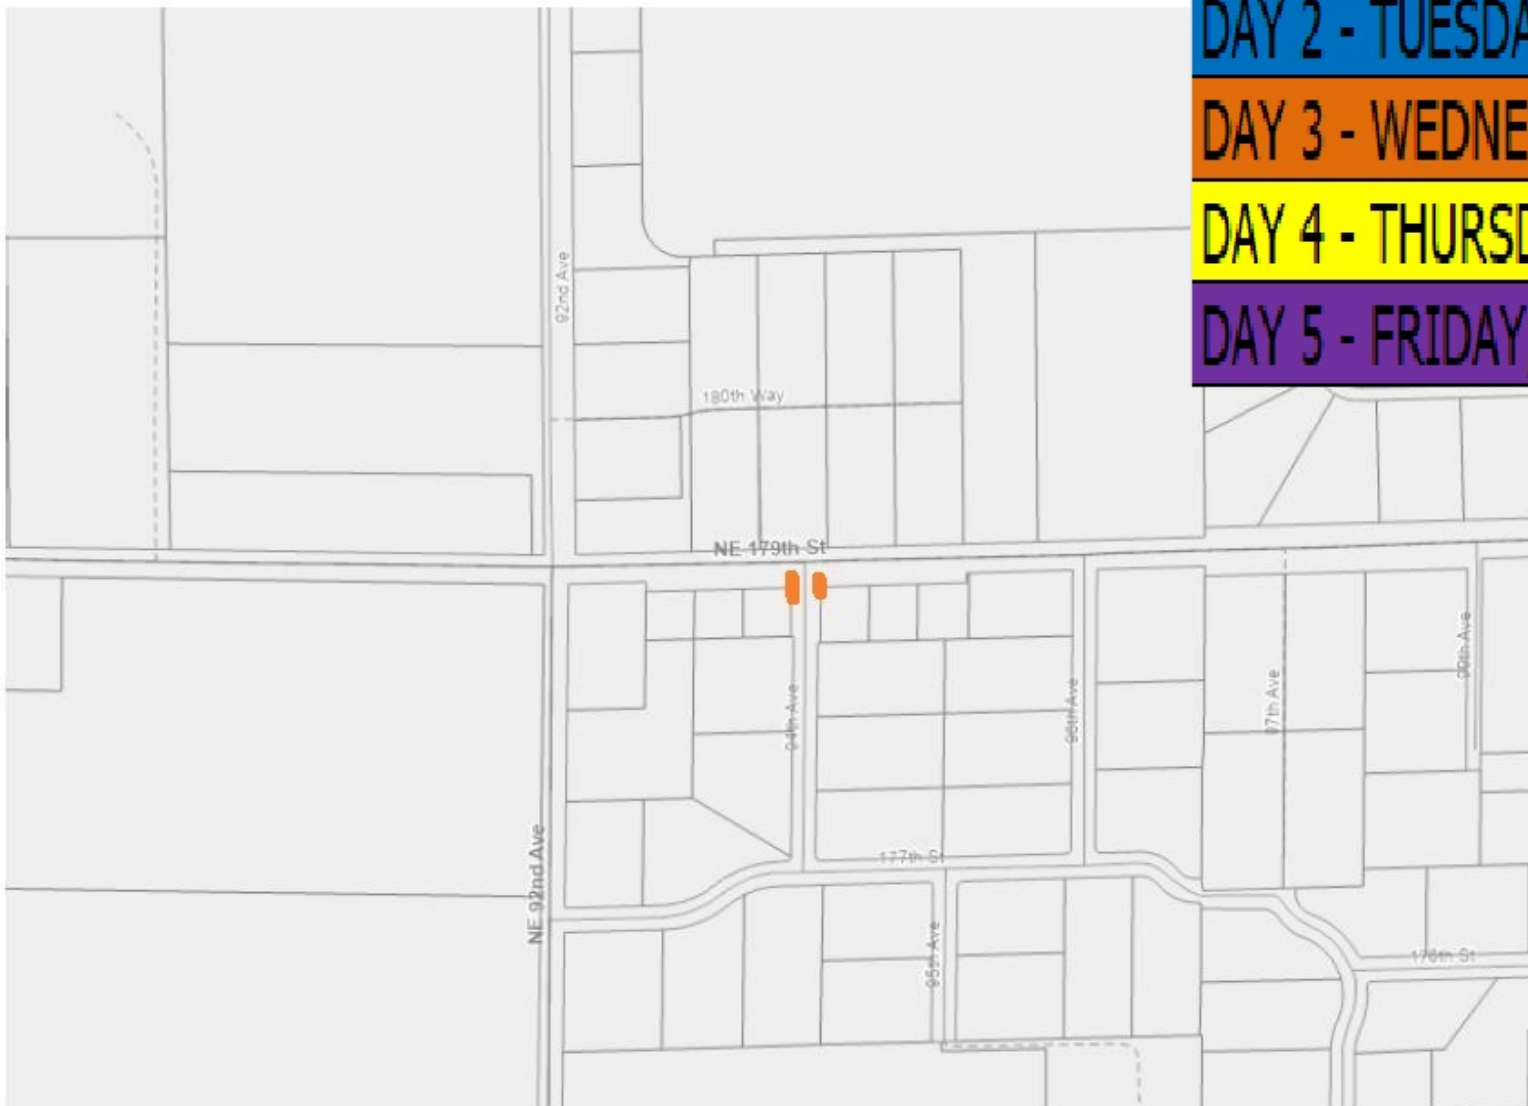

SUBDIVISIONS:
G403 - WESTGLADE - TOUCH UP
FROM 2023

FRIDAY GARBAGE



2024 Joint Agency Slurry Seal Project Map 24-H


DAY 1 - MONDAY, JULY 8TH

DAY 2 - TUESDAY, JULY 9TH

DAY 3 - WEDNESDAY, JULY 10TH

DAY 4 - THURSDAY, JULY 11TH

DAY 5 - FRIDAY, JULY 12TH

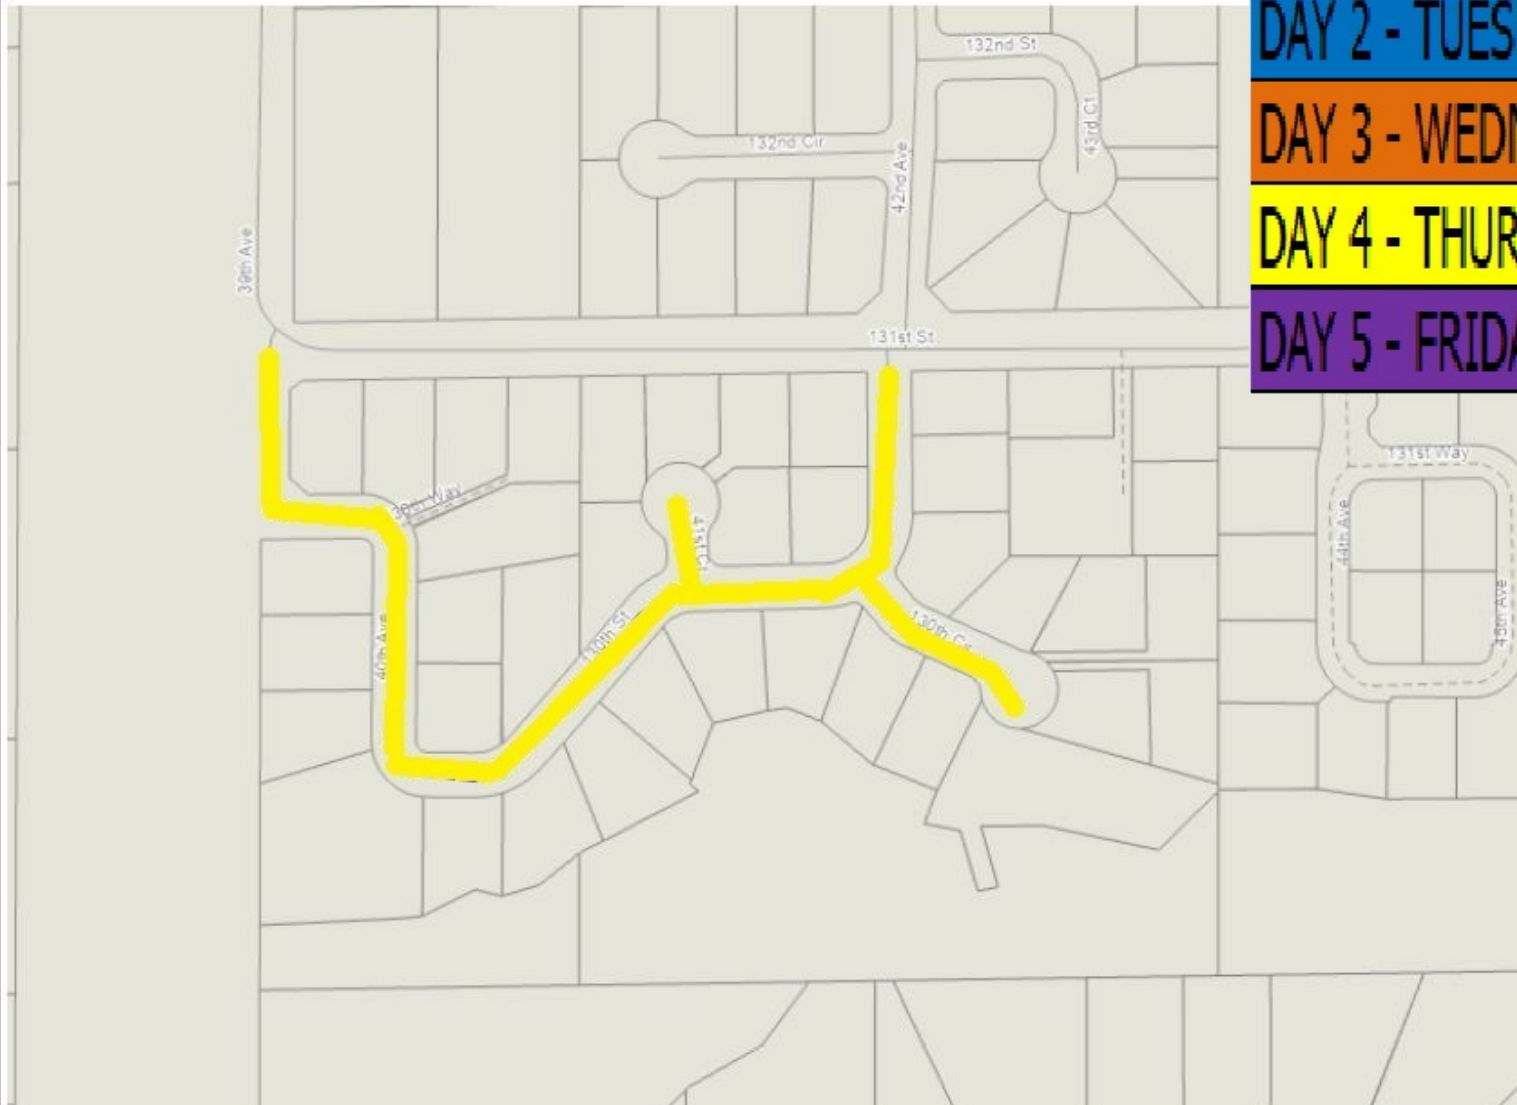

THURSDAY GARBAGE

SUBDIVISIONS:
311333 - CANYON RIDGE
311197 - PLEASANT MEADOW



2024 Joint Agency Slurry Seal Project Map 24-1


DAY 1 - MONDAY, JULY 8TH

DAY 2 - TUESDAY, JULY 9TH

DAY 3 - WEDNESDAY, JULY 10TH

DAY 4 - THURSDAY, JULY 11TH

DAY 5 - FRIDAY, JULY 12TH

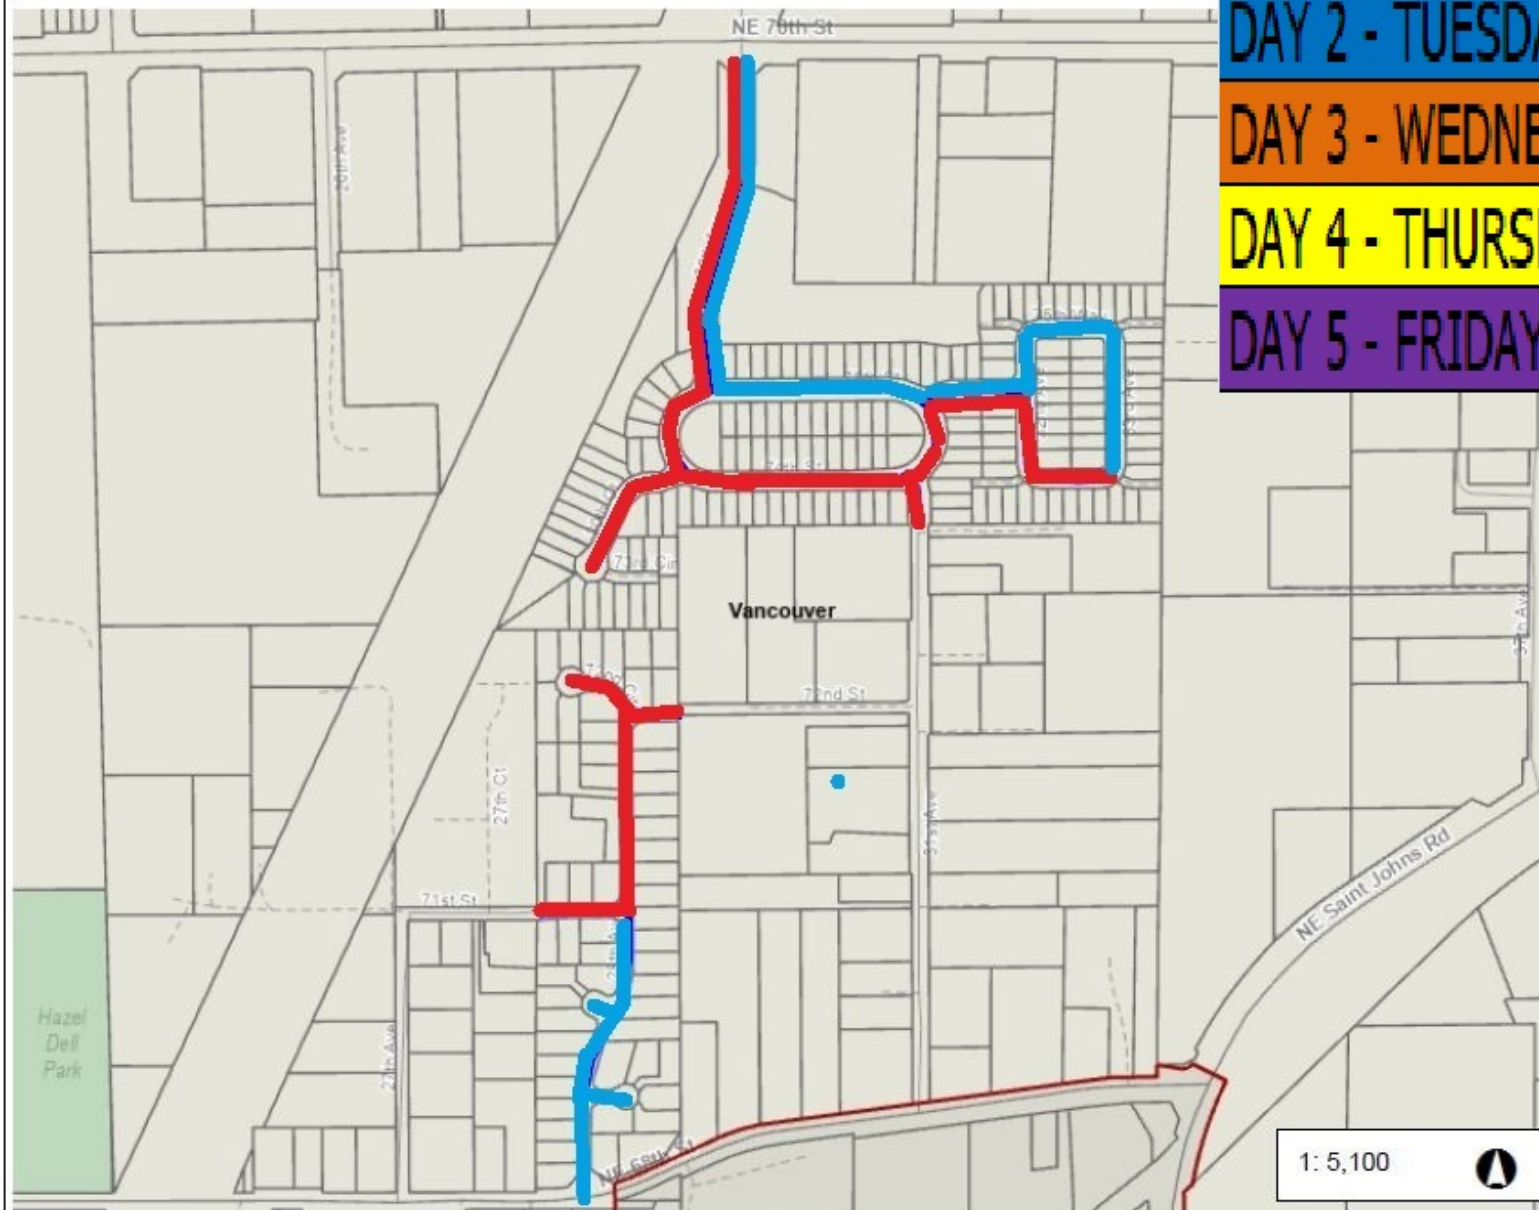

1: 5,100

SUBDIVISIONS:
311736 - HIDDEN GARDENS PH 1
311836 - HIDDEN GARDENS PH 2
311479 - SOUTHVIEW TERRACE

FRIDAY GARBAGE



DAY 1 - MONDAY, JULY 8TH

DAY 2 - TUESDAY, JULY 9TH

DAY 3 - WEDNESDAY, JULY 10TH

DAY 4 - THURSDAY, JULY 11TH

DAY 5 - FRIDAY, JULY 12TH



SUBDIVISIONS:
311638 - BURNT BRIDGE VILLAGE

TUESDAY GARBAGE



2024 Joint Agency Slurry Seal Project Map 24-K


DAY 1 - MONDAY, JULY 8TH

DAY 2 - TUESDAY, JULY 9TH

DAY 3 - WEDNESDAY, JULY 10TH

DAY 4 - THURSDAY, JULY 11TH

DAY 5 - FRIDAY, JULY 12TH

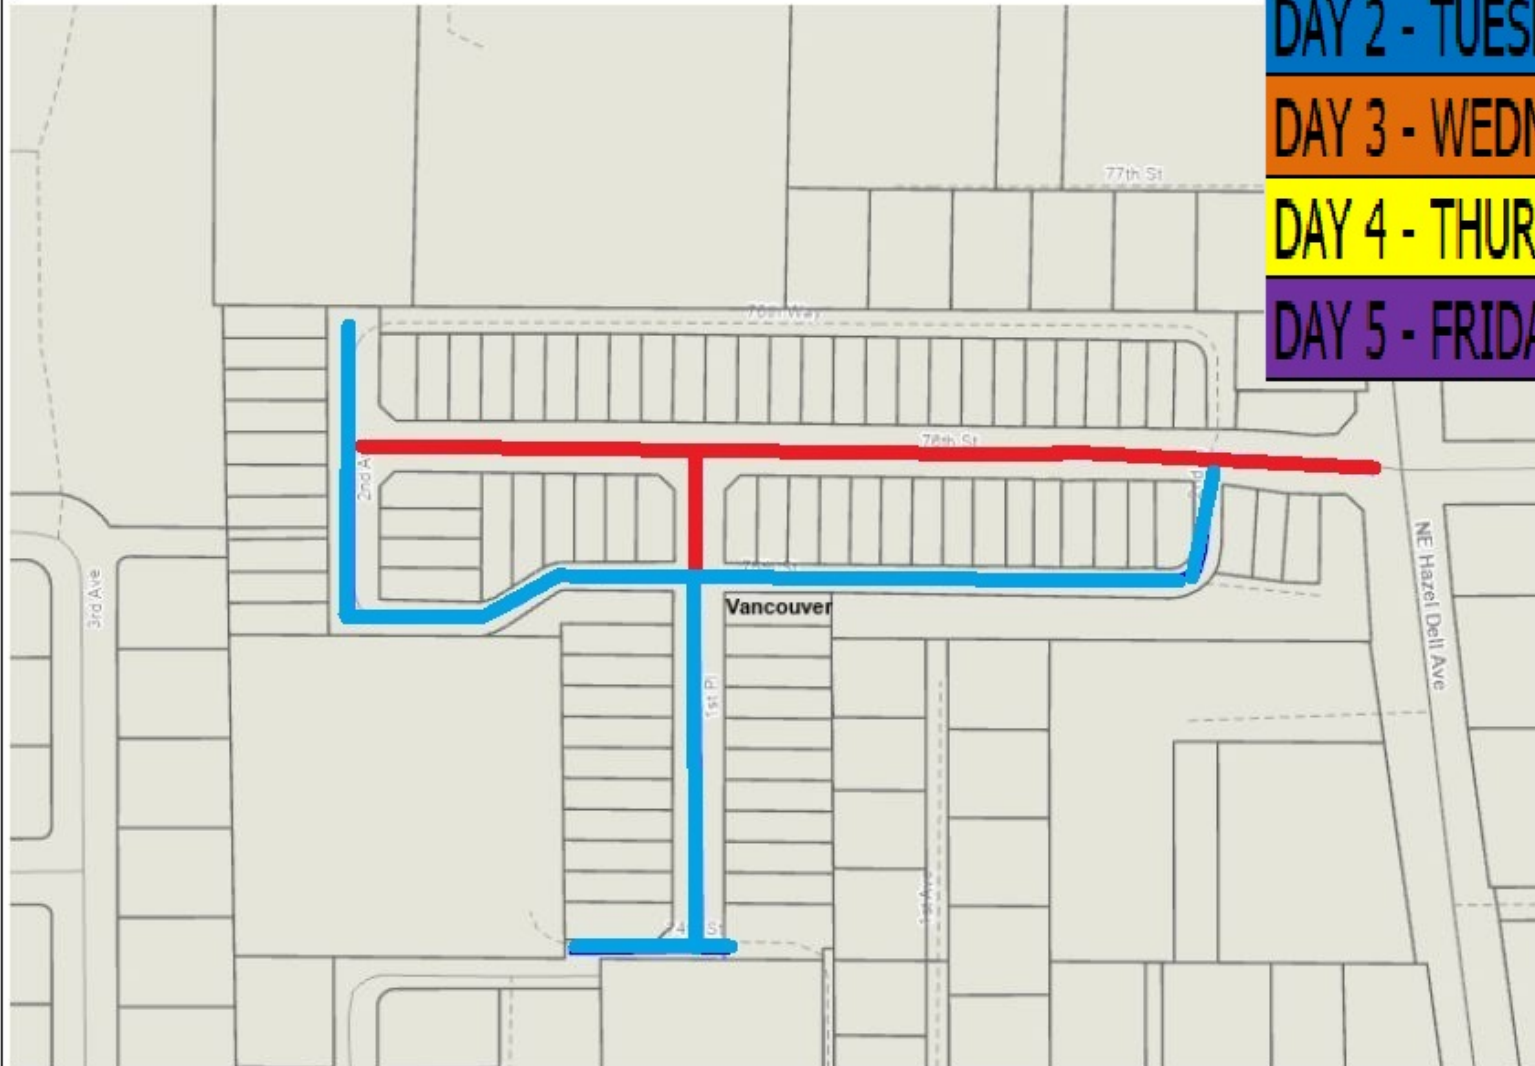

TUESDAY GARBAGE

SUBDIVISIONS:
311568 - HAZEL RIDGE
TOWNHOMES PH 1



2024 Joint Agency Slurry Seal Project Map 24-L


DAY 1 - MONDAY, JULY 8TH

DAY 2 - TUESDAY, JULY 9TH

DAY 3 - WEDNESDAY, JULY 10TH

DAY 4 - THURSDAY, JULY 11TH

DAY 5 - FRIDAY, JULY 12TH

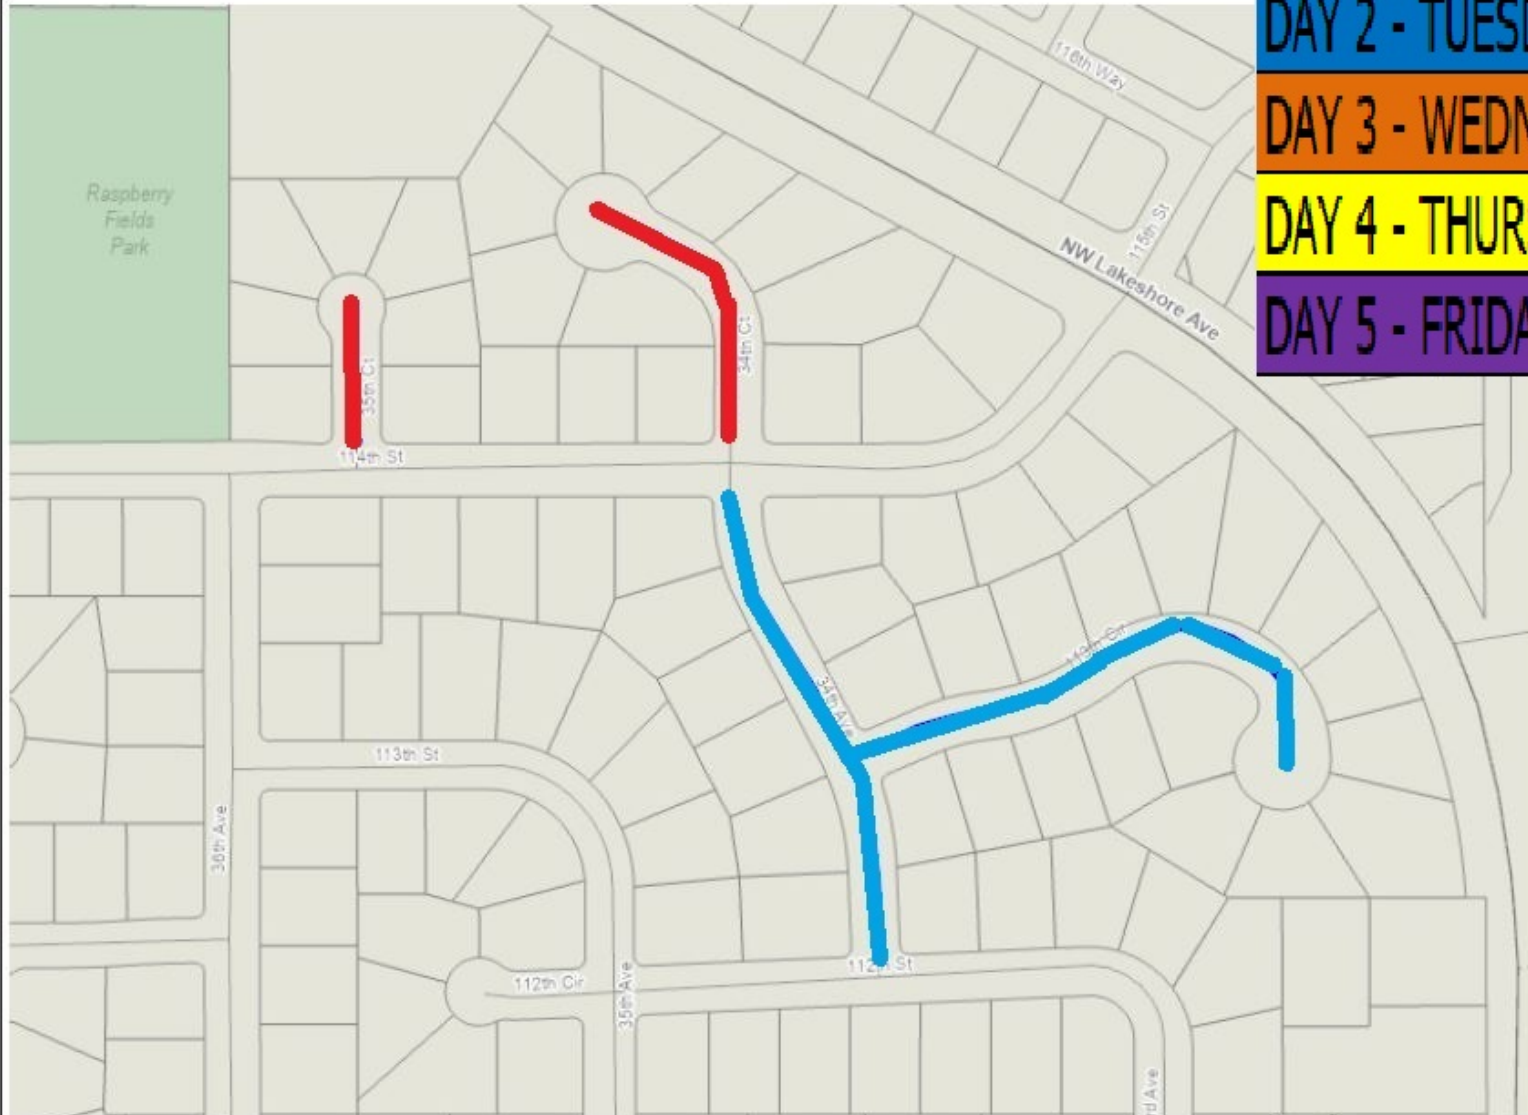

TUESDAY GARBAGE

SUBDIVISIONS:
J194 - WESTMOOR PHASE 2
J240 - WESTMOOR 2 PHASE 2



2024 Joint Agency Slurry Seal Project Map 24-M


DAY 1 - MONDAY, JULY 8TH

DAY 2 - TUESDAY, JULY 9TH

DAY 3 - WEDNESDAY, JULY 10TH

DAY 4 - THURSDAY, JULY 11TH

DAY 5 - FRIDAY, JULY 12TH

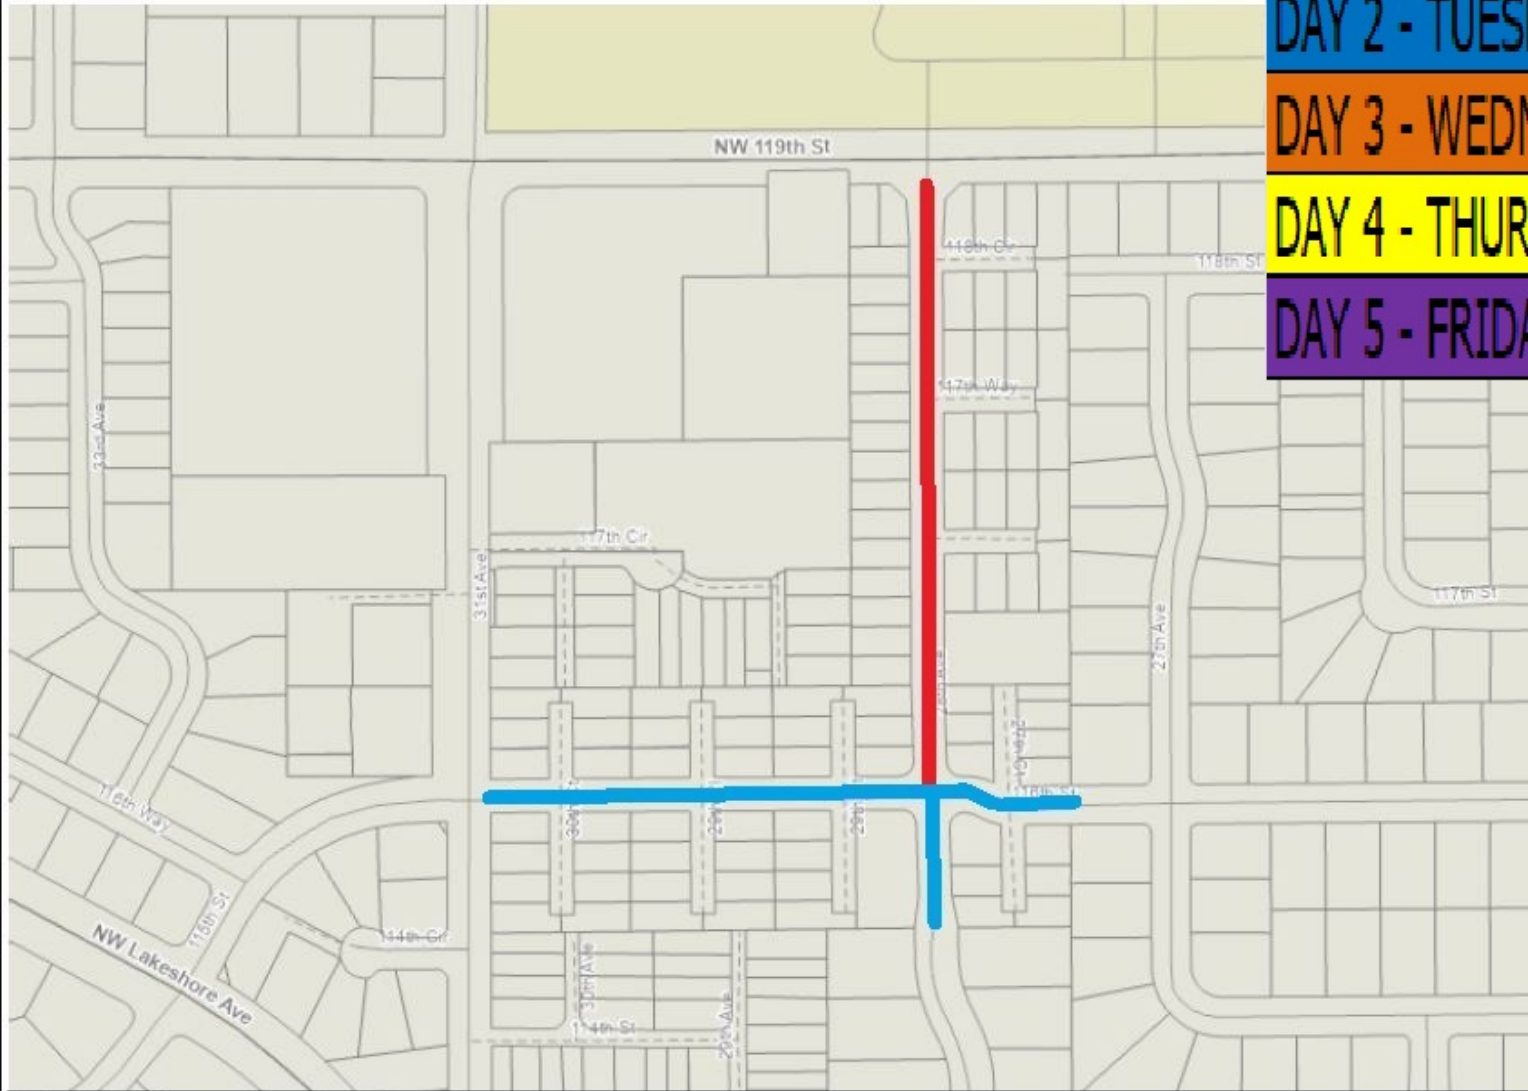

SUBDIVISIONS:
311247 - TIARE PLACE
310887 - FELIDA VIEW

TUESDAY GARBAGE

Project: 2024 JOINT AGENCY SLURRY SEAL PROJECT
 Location: Clark County, WA

Date: Monday, July 8, 2024

DAY 1

GARBAGE STOCKPILE

SQUARE PROJECT

<u>DAY</u>	<u>/ MAP</u>	<u>STREET</u>	<u>FROM</u>	<u>TO</u>	<u>YARDS</u>	<u>SY</u>
Thurs	WEST / M	NW 28th Ave	NW 119th St	NW 116th ST	1,800	1,800
Thurs	WEST / L	NW 35th Ct	NW 114th St	North to End	1,000	1,000
Thurs	WEST / L	NW 34th Ct	NW 114th St	North to End	1,468	1,468
Thurs	WEST / J	NE 4th Ave/ NE 52nd St/Ne 2nd Ave	5098 NE 2nd Ave	NE Newhouse Rd	1,705	1,705
Mon	WEST / A	NE 56th Way	NE 66th Ave	East to End	920	
Mon	WEST / A	NE 67th Ct	NE 56th Way	North to End	241	1,161
Thurs	WEST / I	NE 28th Ave	NE 71st St	North to Cul-De-Sac	2,200	
Thurs	WEST / I	NE 71st ST	Ne 28th Ave	2708 NE 71st ST	500	
Thurs	WEST / I	NE 72nd ST	Ne 28th Ave	Dead End	300	3,000
Thurs	WEST / I	NE 75th St Loop	Ne 30th Ave	NE 30th Ave	3,500	
Thurs	WEST / I	NE 30th Ct	NE 30th Ave	South to end	1,188	
Thurs**	WEST / I	SOUTH SIDE OF NE 75th St	Ne 31st Ave	Ne 32nd Ave	333	
Thurs*	WEST / I	WEST SIDE OF NE 30th Ave	NE 78th St	NE 75th St	1,300	
Thurs	WEST / I	NE 32nd Ave Loop	NE 75th St	NE 75th St	1,129	7,450
Thurs	WEST / K	NW 76th St	NE Hazel Dell Ave	NW 2nd Ave	2,787	
Thurs	WEST / K	NW 1st Pl	NW 76th St	NW 75th ST	331	3,118
TOTAL					20,702	20,702

Notes:

*NE 30th Ave: Complete west side of road

**NE 75th St: Complete South Side of Road

4 FLAGGERS NEEDED AT PROJECT 7 (75TH LOOP)

1 SPOTTER NEEDED AT PROJECT 8 (76TH ST - SEE SMALL MAP)

PLEASE CAUTION TAPE BARRICADES AND PROVIDE DETOURS TOWARD THE SOUTH 1 LANE

ENTRANCE/EXIT AT PROJECT 8 (76TH ST - SEE SMALL MAP)

Project: 2024 JOINT AGENCY SLURRY SEAL PROJECT

Location: Clark County, WA

Date: Tuesday, July 9, 2024

DAY 2

GARBAGE STOCKPILE

SQUARE PROJECT

<u>DAY</u>	<u>/ MAP</u>	<u>STREET</u>	<u>FROM</u>	<u>TO</u>	<u>YARDS</u>	<u>SY</u>
Thurs	WEST / M	NW 28th Ave	Nw 116th St	11416 NW 28th Ave	361	
Tue/Thurs	WEST / M	Nw 116th St	NW 31st Ave	181 ft East NW 28th Ave	3337	3698
Thurs	WEST / L	NW 34th Ave/ NW 113th Cir	NW 112th St	NW 114th St	3602	3602
Thurs	WEST / K	NW 2nd Ave	North to end	South to end	823	
Thurs	WEST / K	NW 1st Pl	NE 75th St	South to end	1100	
Thurs	WEST / K	NW 75th St	NE 76th St	NW 1st Pl	593	
Thurs	WEST / K	NW 75th St	NW 1st Pl	NW 2nd Ave	1064	3580
Thurs	WEST / J	NE 2nd Ave	Ne Newhouse Rd	5098 NE 2nd Ave	400	400
Thurs	WEST / I	NE 28th Ave	NE 68th Ave	NE 71st St	2717	2,717
Thurs	WEST / I	NE 75th St Loop	Ne 30th Ave	NE 30th Ave	1747	
Thurs **	WEST / I	NORTH SIDE OF NE 75th St	Ne 31st Ave	Ne 32nd Ave	333	
Thurs *	WEST / I	EAST SIDE OF NE 30th Ave	NE 78th St	NE 75th St	1283	
Thurs	WEST / I	NE 32nd Ave Loop	NE 75th St	NE 75th St	1800	5163

TOTAL 19,160 19,160

Notes:

*NE 30th Ave: Complete East side of road

**NE 75th St: Complete North Side of Road

4 FLAGGERS NEEDED ON LAST PROJECT

Project: 2024 JOINT AGENCY SLURRY SEAL PROJECT
 Location: Clark County, WA

Date: Wednesday, July 10, 2024

DAY 3

GARBAGISTOCKPILE

				SQUARE	PROJECT	
DAY	/ MAP	STREET	FROM	TO	YARDS	SY
Fri	EAST / F	NE 197th St/NE 196th St/ NE 197th Cir	NE 112th Ave	EAST OF 11015 NE 196TH ST.	7,304	7,304
Fri	EAST / F	NE 116th Ave/NE 186 Cir/Ne 185th St	518 ft S of Ne 189th St	South to end	5,342	5,342
Fri	EAST / F	NE 113th Ave	Ne 189th St	70 ft W of NE 111th Ave	6,346	6,346
Wed	EAST / C	NE 100th Ave	NE 79th St	North to end	3,209	
Wed	EAST / C	NE 81st St	NE 100th Ave	East to end	767	
Wed	EAST / C	NE 79th St	NE 100th Ave	200 ft E of NE 79th St	883	4,859
Fri	EAST / G	NE 94th Ave	West Curb Return	East Curb Return	102	102
Fri	EAST / F	NE 196th St	WORK PERFORMED IN A.M.	NE 112th Ave	1,400	1,400
				TOTAL	25,353	25,353

Notes:

AM/PM 116TH AVE/NE 186TH CIR./NE 185TH ST. PER RIKU'S REQUEST.

Project: 2024 JOINT AGENCY SLURRY SEAL PROJECT
 Location: Clark County, WA

Date: Thursday, July 11, 2024

DAY 4

GARBAGE STOCKPILE

SQUARE PROJECT

<u>DAY</u>	<u>/ MAP</u>	<u>STREET</u>	<u>FROM</u>	<u>TO</u>	<u>YARDS</u>	<u>SY</u>
Friday	EAST / H	NE 40th Ave/NE 130th St	NE 131st St	214 ft W of NE 40th Ave	2,151	
Friday	EAST / H	NE 130th St/NE 42nd Ave	214 ft W of NE 40th Ave	NE 131st St	1,758	
Friday	EAST / H	NE 41st Ct	NE 130th St	north to end	553	
Friday	EAST / H	NE 130th Cir	NE 130th St	South to end	879	5,341
Fri	EAST / D	NE 86th Cir	NE 88th St	South to Cul-De-Sac	1,315	1,315
Wed	EAST / C	NE 71st St	NE 100th Ave	1/2 INT. @ NE 102nd Ct	2,884	
Wed	EAST / C	NE 101st Ave	7215 NE 101st Ave	South to Cul-De-Sac	2,800	5,684
Wed	EAST / E	NE 88th St	NE 107th Ave	104ft E of NE 110th Ave	3,010	
Wed	EAST / E	NE 110th Ave	NE 99th St	105ft S NE 97th St	400	3,410
Wed	EAST / E	NE 93rd St	NE 110th Ave	NE 112th Ave	2,021	
Wed	EAST / E	NE 111th Ave	NE 93rd St	150 ft South of NE 92nd Cir	2,139	
Wed	EAST / E	NE 92nd Cir	NE 111th Ave	East to end	1,048	
Wed	EAST / E	NE 112th Ave	NE 93rd St	120ft North	427	5,635
Wed	EAST / E	NE 98th St/ NE 111th Ave/NE 97th St	NE 110th Ave	NE 110th Ave	3,282	
Wed	EAST / E	NE 97th St	NE 110th Ave	145 ft W of NE 110th Ave	499	
Wed	EAST / E	NE97th St/NE 108th Ct	145 Ft W of NE 110th Ave	East/North to End	1,693	5,474
Mon	EAST / B	HALF OF ENTRANCE NE 64th PL + NE 10	NE 107th Ave	Loop To NE 65th St	1,911	1,911
TOTAL					28,770	28,770

Notes:

Project: 2024 JOINT AGENCY SLURRY SEAL PROJECT
 Location: Clark County, WA

Date: Friday, July 12, 2024

DAY 5

GARBAGE STOCKPILE

SQUARE PROJECT

<u>DAY</u>	<u>/ MAP</u>	<u>STREET</u>	<u>FROM</u>	<u>TO</u>	<u>YARDS</u>	<u>SY</u>
Mon	EAST / B	NORTH HALF OF ENTRANCE + NE 65th St + NE 108th Ave	NE 107th Ave	Loop To NE 65th St	2,200	2,200
Wed	EAST / C	NE 75th St/ NE 108th Ave/ NE 108th Ct	NE 107th Ave	100 ft E NE 108th Ave	4,300	
Wed	EAST / C	NE 108th Ave	Cul-De-Sac	South to end	436	4,736
Wed	EAST / E	NE 110th Ave	NE 99th St	NE 97th St	2,402	2,402
Wed	EAST / C	NE 100th Ave	NE 79th St	NE 76th St	4,053	4,053
Wed	EAST / C	NE 70th St	NE 102nd Ave	East to end	1,028	
Wed	EAST / C	NE 102nd Ave	NE 71st St	South to end	3,096	
Wed	EAST / C	NE 103rd Ave/ NE 71st St	1/2 INT @ NE 102nd Ct	140 E of NE 103rd Ave	2,536	
Wed	EAST / C	NE 69th St	NE 102nd Ave	East to end	852	7,512
Mon	EAST / B	NE 100th Ave	145 Ft N of NE 62nd Cir	135 Ft S of NE 61st Cir	1,836	
Mon	EAST / B	NE 61st St	135 Ft W of NE 100th Ave	NE 100th Ave	585	
Mon	EAST / B	NE 62nd Cir	NE 100th Ave	East to end	1,183	
Mon	EAST / B	NE 61st Cir	NE 100th Ave	East to end	1,183	
Mon	EAST / B	NE 100th Ave	NE 63rd St	130 Ft South	405	5,192
Mon	EAST / B	NE 58th St	NE 102nd Ave	East to end	1,002	1,002
Mon	EAST / B	NE 104th Pl	NE Covington Rd	South To New Pavement	1,062	1,062
TOTAL					28,159	28,159

Notes:

AM/PM REQUIRES 2 FLAGGERS
